



**CHINO VALLEY UNIFIED SCHOOL DISTRICT
WOODCREST JUNIOR HIGH SCHOOL
NEW CONSTRUCTION**

**CONSTRUCTION STATUS REPORT
DECEMBER 2006**

1- PROJECT DESCRIPTION

Start Date: March 5, 2003 Start of Construction
Finish Date: August 25, 2005 Substantial Completion
Scope: New Construction Junior High School

2- PROJECT STATISTICS

- Site Acreage – 8.40
- Parking Lot(s) / Stalls – 2 / 59
- Building(s) – 4 / 73,205
- Classroom(s) – 26
- Football Field(s) – 0
- Running Track(s) – 0
- Soccer Field(s) – Joint use
- Tennis Court(s) – 0
- Basketball Court(s) – 11 8 out; 3 in
- Baseball / Softball Field(s) – Joint use
- Volleyball Court(s) – 6 4 out; 2 in
- Badminton Court(s) – 6

3- SCHEDULE STATUS

- School is occupied.
- Punch list items are in progress. Incomplete Contract work has been isolated.
- Woodcrest JHS was officially dedicated on January 23, 2006.
- Low Voltage at Modulers in progress
- Offsite work complete
- DSA Closeout work pending budgetary considerations and bid process

4- CLAIMS STATUS

- One remaining claim – ISEC – In resolution

5- NEXT 30 DAY PROGRESS PROJECTION

- **DSA/ Non-Contract Completion Bid:** NTD to have bid package prepared by 10/20
- **Offsite:** Construction complete
- **Punch list:** In progress.
- **Closeout:** Duray, ISEC, Not yet complete

Photos:


(Following Page)




**CHINO VALLEY UNIFIED SCHOOL DISTRICT
WOODCREST JUNIOR HIGH SCHOOL
NEW CONSTRUCTION**

**CONSTRUCTION STATUS REPORT
DECEMBER 2006**

FRONT OF SCHOOL FROM CAMPUS

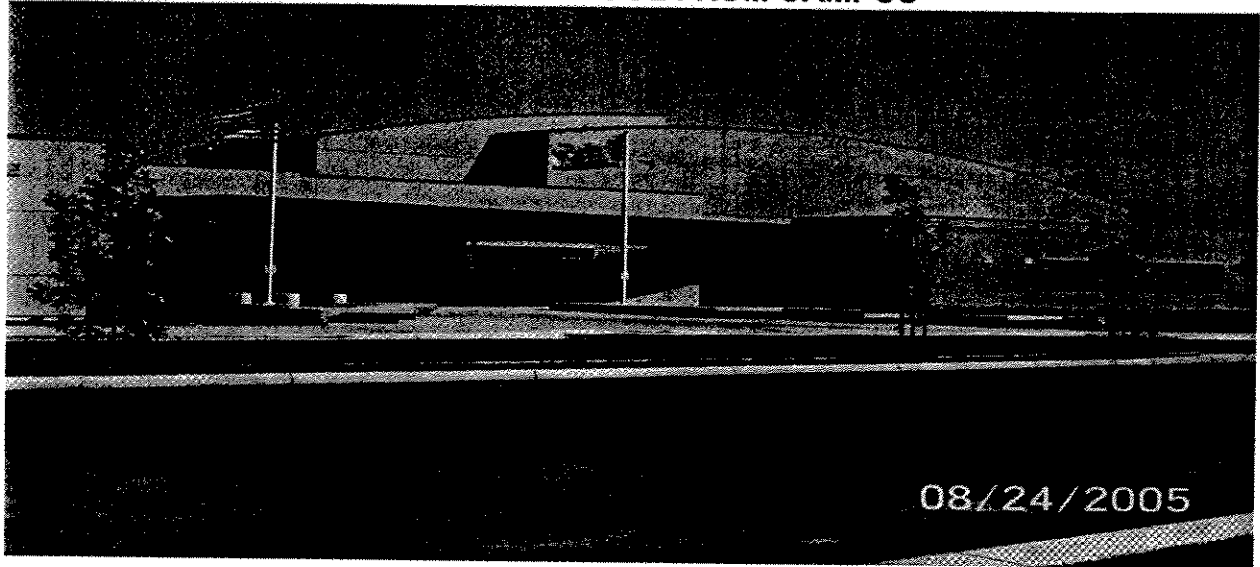

FROM SOUTH WEST CORNER OF CAMPUS

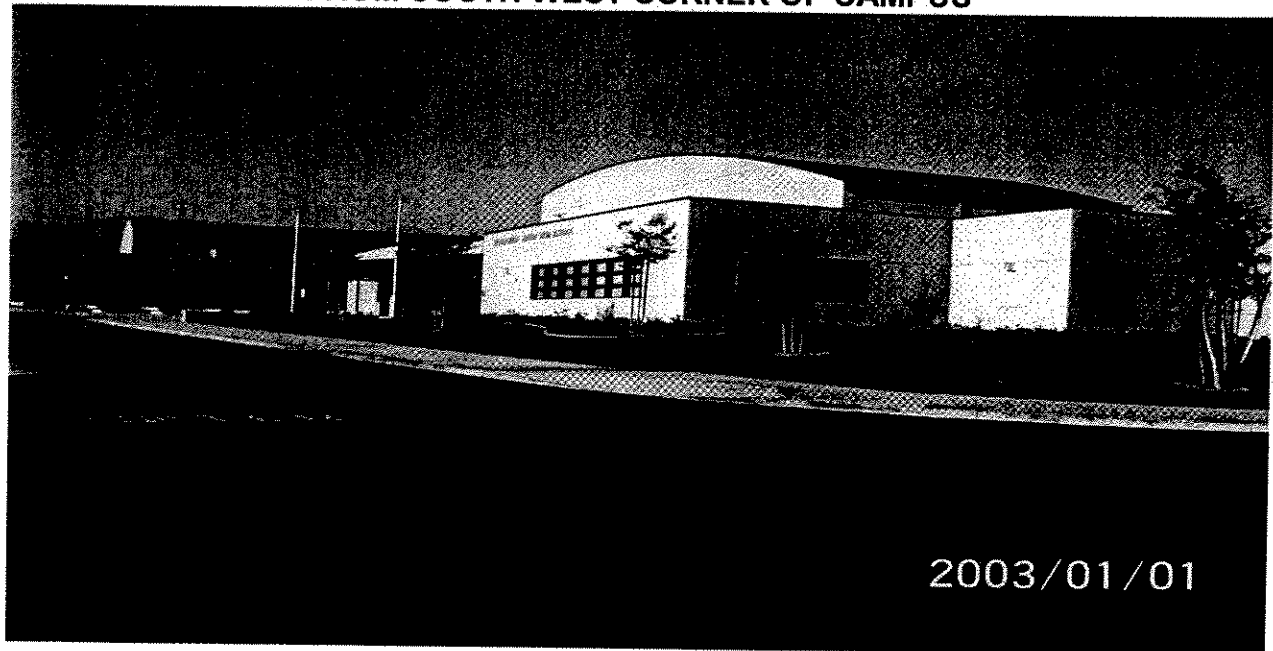

6- COST-

- Budget Cost Report: See following page




**CHINO VALLEY UNIFIED SCHOOL DISTRICT
WOODCREST JUNIOR HIGH SCHOOL
NEW CONSTRUCTION**

**CONSTRUCTION STATUS REPORT
DECEMBER 2006**

Updated January 25, 2006		ORIGINAL CONTRACT	APPROVED C.O. / P.O. TO DATE	CURRENT CONTRACT DATE TO DATE	PENDING C.O. NOT AWARDED COSTS	FORECAST C.O. REMAINING WORK	FORECAST TOTAL WORK
		(B)	(C)	(D)	(E)	(F)	(G = D + E + F)
	WOODCREST JHS						
1	BOGH	\$ 2,895,000.00	\$ 92,841.00	\$ 2,987,841.00			\$ 3,134,922.78
3	PERSALL	\$ 455,000.00	(10,885.00)	\$ 444,115			\$ 444,115.00
4	COLUMBIA	\$ 1,457,700.00	\$ 24,111.00	\$ 1,481,811.00			\$ 1,481,811.00
5	GAMUT	\$ 1,315,000.00	\$ 27,175.79	\$ 1,342,175.79			\$ 1,342,175.79
6	ISEC	\$ 683,333.00	\$ (22,840.00)	\$ 660,493.00			\$ 669,211.28
7	STOLO	\$ 499,000.00	\$ 32,995	\$ 486,008.00			\$ 531,395.00
8	BELL ROOF	\$ 306,578.00	\$ (5,853.00)	\$ 300,725.00			\$ 300,725.00
9	CROWNER	\$ 818,000.00	\$ 27,489.00	\$ 845,489.00			\$ 845,489.00
10	SIERRA	\$ 890,000.00	\$ 68,179.49	\$ 958,179.49			\$ 958,179.49
11	PADUA	\$ 70,740.00	\$ 2,162.66	\$ 72,902.66			\$ 72,902.66
12	ANGELES	\$ 211,000.00	\$ 532.66	\$ 211,532.66			\$ 211,532.66
13	INLAND	\$ 163,550.00	\$ 14,556.00	\$ 178,106.00			\$ 178,106.00
14	DM HOOVER	\$ 271,995.00	\$ 583.00	\$ 272,578.00			\$ 272,578.00
15	SIMMONS	\$ 300,000.00	\$ 21,054.00	\$ 321,054.00			\$ 321,054.00
16	BERT	\$ 578,000.00	\$ 90,568.23	\$ 668,568.23			\$ 668,568.23
17	NOT USED						
18	DURAY	\$ 305,000.00		\$ 305,000.00			\$ 305,000.00

[illegible]

Page 4 of 5

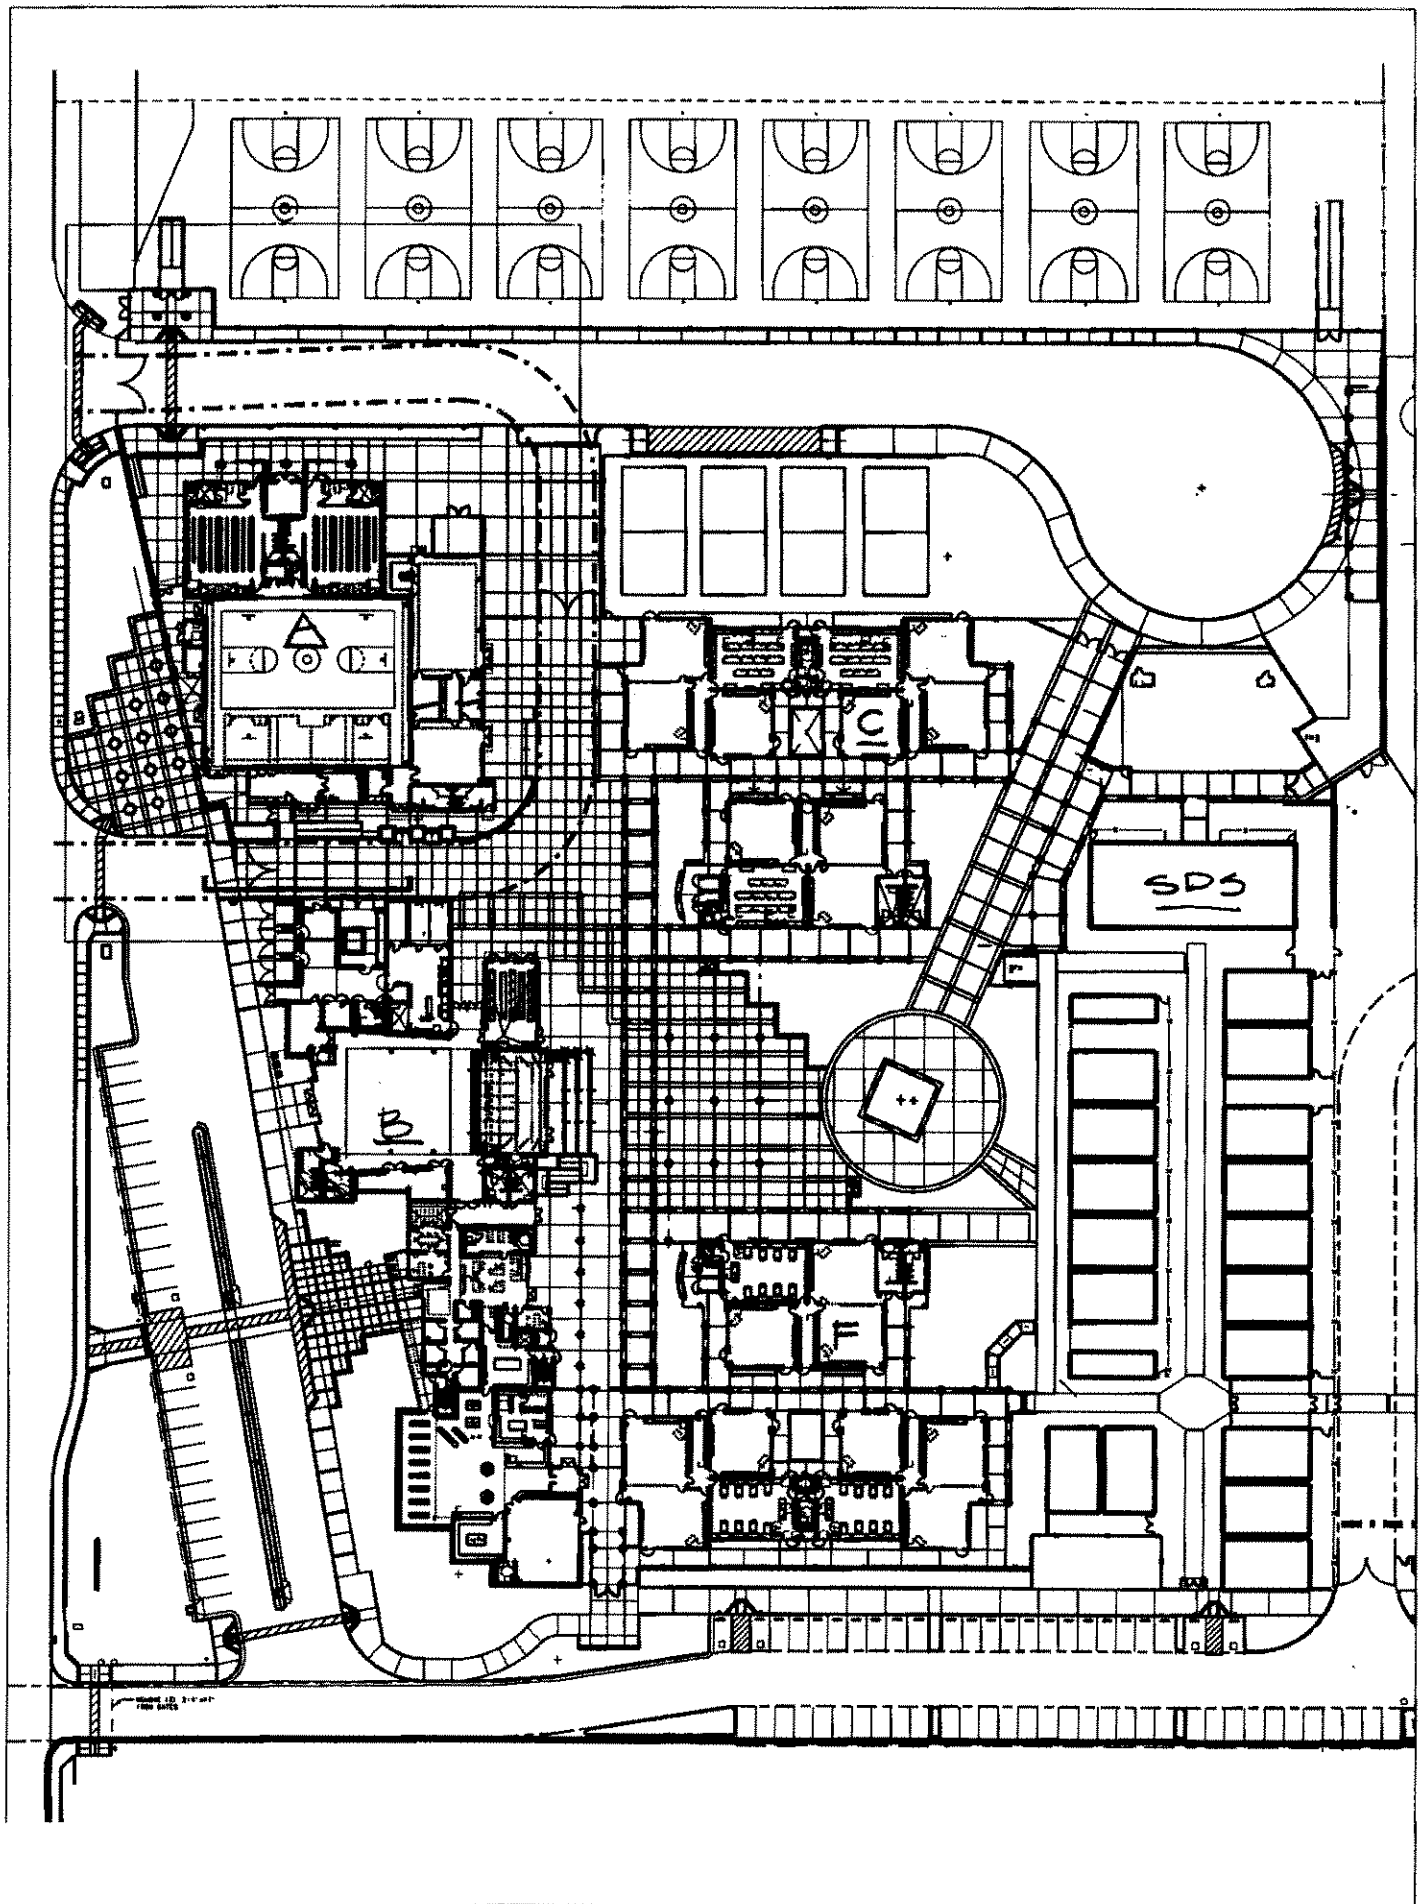

Woodcrest Junior High
